



## Partner Reporting Form

This report should be based on the approved project proposal. It is the partner's responsibility to ensure accuracy of reporting. Reports should be submitted at regular intervals agreed at the funding award stage.

Project Information:	
<b>Project Title:</b>	<b>Building a field hospital in Tell-Temer</b>
<b>Partner Name:</b>	Kurdish Red Crescent
<b>Country:</b>	<b>Syria</b>
<b>Areas of implementation</b> (Governorate, District)	<b>Governorate : Al Hasakeh</b> <b>District : Tel-Temer</b>
<b>Sector(s):</b>	<b>healthy Sector</b>
<b>Budget Total:</b> Cash: GIK:	<b>250,450 €</b>
<b>Report Type:</b> ( Interim/ Final)	<i>Interim report</i>
<b>Reporting Period:</b>	<i>Monthly (November)</i>
<b>Report submitted By:</b> (Name & Position)	<b>Emgiyan Shawish : (monitoring,evaluation,accountability,learning) reporter</b>
<b>Submission Date:</b>	<b>1-31/1/2016</b>

Progress Report	
<b>Update to Project Context:</b> Any changes in the area of implementation that are important to the project	<p><b>R1: chosing a location of building</b> making the basic meeting to discuss the important matters.</p> <p><b>R2: in the second month of project,we did the basic activities such as demolition , cracking, casting of the bases of the building. We will countinu what are remaining of the demonaitation operation in December month .</b></p> <p><b>R3: in the third month have done</b></p>
<b>Project Goal:</b>	Building a filde of hospital in Tel-Temer , to serve more than 50,000 person of population in this town, the villages , and the countrysides also of Tel-Temer area .
<b>Objectives:</b>	<p><b><u>Objective 1 : Project start-up activities:</u></b></p> <p><b>Project kick off meeting:</b></p> <p>1- Project kick off meeting:</p> <p>The basic meetings were done in the 1<sup>st</sup> month :</p>



- **The 1<sup>st</sup> meeting** took place to discuss the work planning of the project and its steps, during the meeting have been select members of the managing committee to follow the project.

2- **Community kick off meeting:** on 11<sup>th</sup> of October 2016 was the **2<sup>nd</sup> meeting**, the managing committee went to Til-temir and they sighted the location of hospital. They did community kick off meeting there, also two members of MSF attended the meeting with local committee, had a look on the location as well, may be **MSF** advanced supports for the project

3- Needs assessment

**Objective 1: to provide the hospital in Tell temir with the secondary health care needed basic.**

**-the hospital will be prepared with secondary health care basic equipment's in which to serve more than 50,000 of the population and IDPS .**

**1- Establish a committee(7 members) involving doctors, engineers and local authorities members (together with KRC):** The managing committee consist of 7members involved (2 Doctors, 2 engineers, Financial expert, Logistic member, Mealing member ), addition to a special staff who work coordination with the managing committee such ( HR, no changes in this side ( second month)

**-NO changes in this side (fourth month)**

**2- make a study in consultation with the committee and expert engineers about the rehabilitation needs;** the managing committee limited an appointment with a civil engineer and an architect to explain to us the planning of building renovation.

**3- In consultation with the committee, identify a suitable building for the new hospital;**

the building that have chosen to be a hospital is an ancient clinic and we will do expansion to ancient clinic, to become reasonable building of hospital

-the ancient clinic has needed to crack of ground and exfoliation of walls.



**4- start the activities of rehabilitation and preparing the building. . . In the last day, the workers started with their job ( rehabilitation of building )**

the logistic officer brought all bricklayer's tools to the project land and the workers started with their job, in another side , other group of workers started to prepre for the new building that will be integral of ancient building, the implementations to build a new building have prepered to work ,

**The workers have finished:**

- cracking of the ground
- Demolition of the ancient wall.
- the wall exfoliation of building.

Some of The amounts of cement,grit , sand ,and cast iron have bought by our logistic , supervisor and engineers ( the details of these materials will preparing by our financial officer )

-casting of holes has done for a new building ( 31 holes )

- number of the workers were 26 ( 6 cracking , 6 exfoliation , 9 casting ).

-During December, we have done what remain of cracking and exfoliation ...etc

- cracking of ceramics that inside the ancient building, copmletion of ceramics exfoliation, number of the workers were (5 workers)

-transfer of the ceramic remains that have crushed

-digging of the beams of the new building meantime the digging the workers have faced old beams of the ancient building exfoliation of the beams of the old building, the number of the workers were (5 workers).

-put the kink of iron in the holes

-the workers of sanitary sewer have started their work in the ancient building

-casting of the beams the number of rows were(5 rows, 58.3 longitudinal) for this casting have done consuming of 139 cement bags.

-filling soil up above the casting basic

-casting the beams of the out building of the operation room

-bring the breaking small stone to the project land for adjustement to distribute it in the land of new building.



	<p>-finishing the sanitary for the both building ( new building and old building).</p> <p>-casting the cement in the land of new building.</p> <p>-casting the cement of the columns of new building (32 columnnes)</p> <p>-buying the bloch (750 blochs ,size 10 cm -- 500 blochs ,size 15 cm)</p> <p><b>Objective 2: provide the population and the IDPS in Tell temr with the secondary health care.</b></p> <p>-start to receive emergency cases , General surgery and Gynaecology ,with the selected medical team that needed for the operation room:</p> <p>Dr.Sherwan has prepared a schedule with list what we need for clinic consiste of two Gynaencologists and two nurses who will work in this hospital .</p> <p>-provide the hospital with tow ambulance to transport the patient to other hospitals in Jazeera Canton for cases that need other treatment such as (CT scan, MRI, higher Surgeries)</p>
	<p>*The blue color refers to what have been done in the previous month</p> <p>*The red color refers to what have been done in the present month</p>
<p><b>Changes:</b> Include any changes to the original proposal &amp; rationale, justifications for variance from targets</p>	<p>During four months ago, we don't faced any changes that change the activities of the project or its goal</p>

<b>Financial Report</b>	
<p><b>Justify any major variances from the agreed budget</b></p>	<p>The details in this context, we'll mention it in the financial report that prepared by our financial officer of the project.</p>

<b>Monitoring, Evaluation, Accountability and Learning (MEAL)</b>	
<p><b>Describe efforts undertaken to monitor the project</b></p>	<p>- the Kurdish Red Crescent continued their activities in the fourth month</p> <p>- the mealing teams are making countinous evaluation and feed backs to know about the progress of project, involved in the project ideas.</p>
<p><b>Describe efforts to ensure accountability to beneficiaries</b></p>	<p>- the committee make a meetings every week to follow up the activities instance the manager of project or one member's project to discuss the progress and changes in work context, and preparation to start the next step of the project.</p>




### Challenges and Lessons Learned

**Major constraints or problems encountered:** How have these been dealt with?

- the car has broken down for many days, that's why we rent a care to transfer from sere kaniye to tell temer
- the weather factory was a reason to make us late in the building.

These are some photos when the workers did their activities:



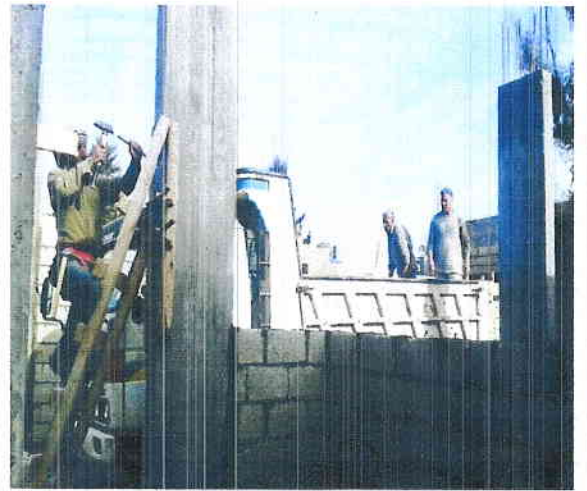

Project manager

Ciwan Mistefa



MEAL Reporter

Emgiyan Shawish

Kornish district – Eben Hesham Street , Building Number 12

[www.HSkurd.org](http://www.HSkurd.org)

Al-Qamishli (ROJAVA) – Syria Tel: +963 52 430 700 +963 993 807 303

[info@HSkurd.org](mailto:info@HSkurd.org)
